

# **WREGIS Town Hall**

**Andrea Coon**  
*Director, WREGIS*


**Electric Reliability  
& Security for the West**

May 20, 2026



# Current Software System Issues

Category	Count
Generation	31
Certificates & Transactions	39
Generators	33
Organization	25
Program	9
DGGs	13
e-Tags	7
Accounts	6
Reports	2
<b>Total</b>	<b>165</b>

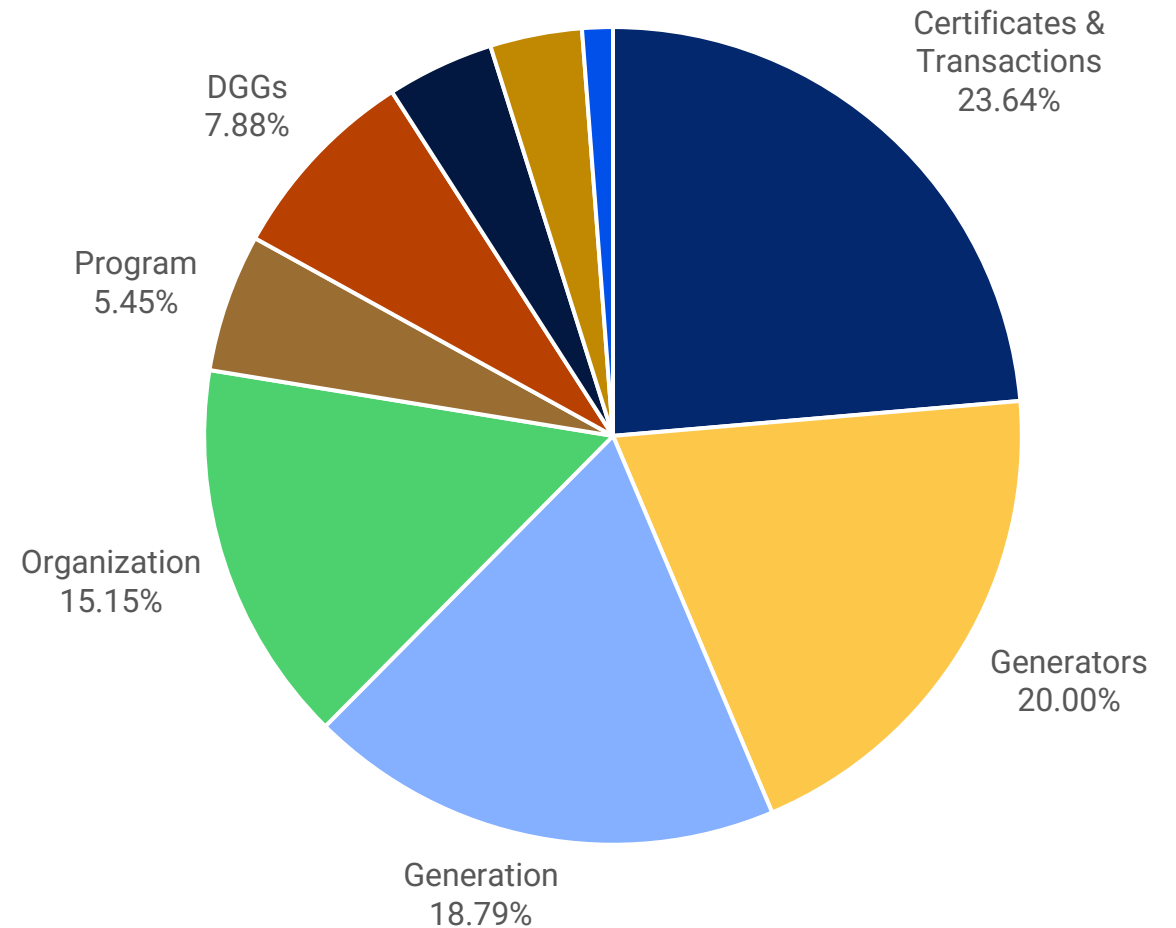



# WREGIS Platform: Phase 1 Development Timeline






# Software Development: Phase 1

- **Q1 2026**

- ✓ Milestone 1 – Established a secure platform foundation with user management features
  - Milestone 2 – Developed the core generator registration system

- **Q2 2026**

- Milestone 3 – Initiating development of the core generation data features
- Milestone 4 – Beginning work on the core Account and Certificate features

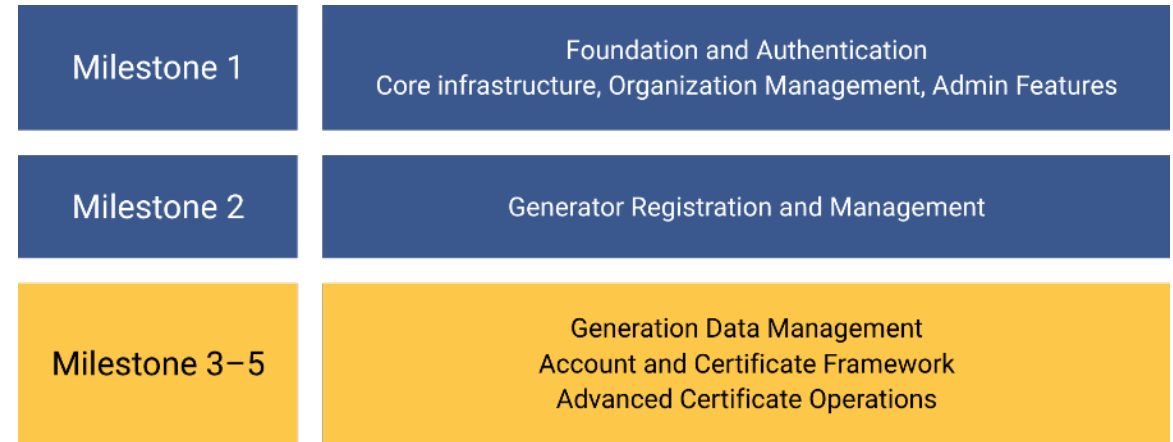



# Milestone 1: Foundation and Authentication (Complete)

Milestone 1

Foundation and Authentication  
Core infrastructure, Organization Management, Admin Features

- **User Management and Security**
  - ✓ Password reset functionality
  - ✓ Multi-factor authentication for enhanced security
  - ✓ Add new users within an organization
  - ✓ Update user privileges and profiles
- **Organization Registration**
  - ✓ Register new customers and QREs
  - ✓ Update organization contact and billing details



# Milestone 2: Generator Registration and Management

- **Generator Management Features**

Milestone 2

Generator Registration and Management

- Register generators
- Update information for approved generators
- Upload and manage generator documentation
- Create and maintain Shared Meter Groups (previously "Aggregated Meter Groups")
- Assign a QRE for generation data reporting
- Track certificate remainder history by fuel type
- Add multiple fuel types to generators



## Milestone 3: Generation Data Management

- Data reporting through UI and file upload
- Meter and fuel type allocations
- Generation activity logging
- Feasibility calculations for data validation
- Adjustments to generation data
- View previously entered allocations

Milestone 3–5

Generation Data Management  
Account and Certificate Framework  
Advanced Certificate Operations



# Milestone 4: Account and Certificate Framework

- **Accounts**

- Create Active, Retirement, and Reserve accounts
- Account reporting

Milestone 3–5

Generation Data Management  
Account and Certificate Framework  
Advanced Certificate Operations

- **Certificates**

- Transferring certificates between accounts
- Retiring certificates
- Reserving certificates
- Recurring transfers
- Mass certificate transfers (via upload file)



# Upcoming Phase 1 Milestones: Later in 2026

- **Q3 2026 – Milestones 5–8**

- Complete remaining Phase 1 platform functionality
- Development prioritization for Milestones 5–8 will be finalized in the coming months, focusing on items of higher complexity
- External user testing planned for Q3, with Atomic Object guiding representative user participation, group selection, and size
- Objective: Align user testing with meaningful functionality while ensuring time to incorporate feedback before launch

Milestone 3–5	Generation Data Management Account and Certificate Framework Advanced Certificate Operations
Milestone 6–8	Program Management and E-Tags Reporting and Analytics API and Integrations
Milestone 9	Quality Assurance and User Acceptance Testing
Milestone 10	Go Live and Support

- **Q4 2026 – Milestones 9–10**

- User Acceptance Testing (UAT): Validate the production-ready environment
- Launch new platform and stabilization



# WREGIS Platform: Phase 1 Development Timeline



# Software Launch Forum (SWLF)

Provides a representative group of active users visibility into the development of the new software.

- Increases transparency of the process
- Strengthens trust with stakeholders
- Builds excitement about the capabilities

**Clarissa Allen** – Bonneville Power Association

**Simon Chang** – Southern California Edison

**Nathan Gallegos** – LA Department of Water and Power

**Matthew Kraai** – Tesla

**Sean Inaba** – California Energy Commission

**Chris Leyerle** – Puget Sound Energy

**Austin Scharff** – Washington Department of Commerce

**Trey Whiting** – Salt River Project

# First SWLF Meeting

---

- First meeting held May 19, 2026
  - All 8 members in attendance
  - Introductions
  - Software timeline
  - Agile 101






# WREGIS Survey Results


Would you support moving the target release date to February 2027?

Answered: 82 Skipped: 1

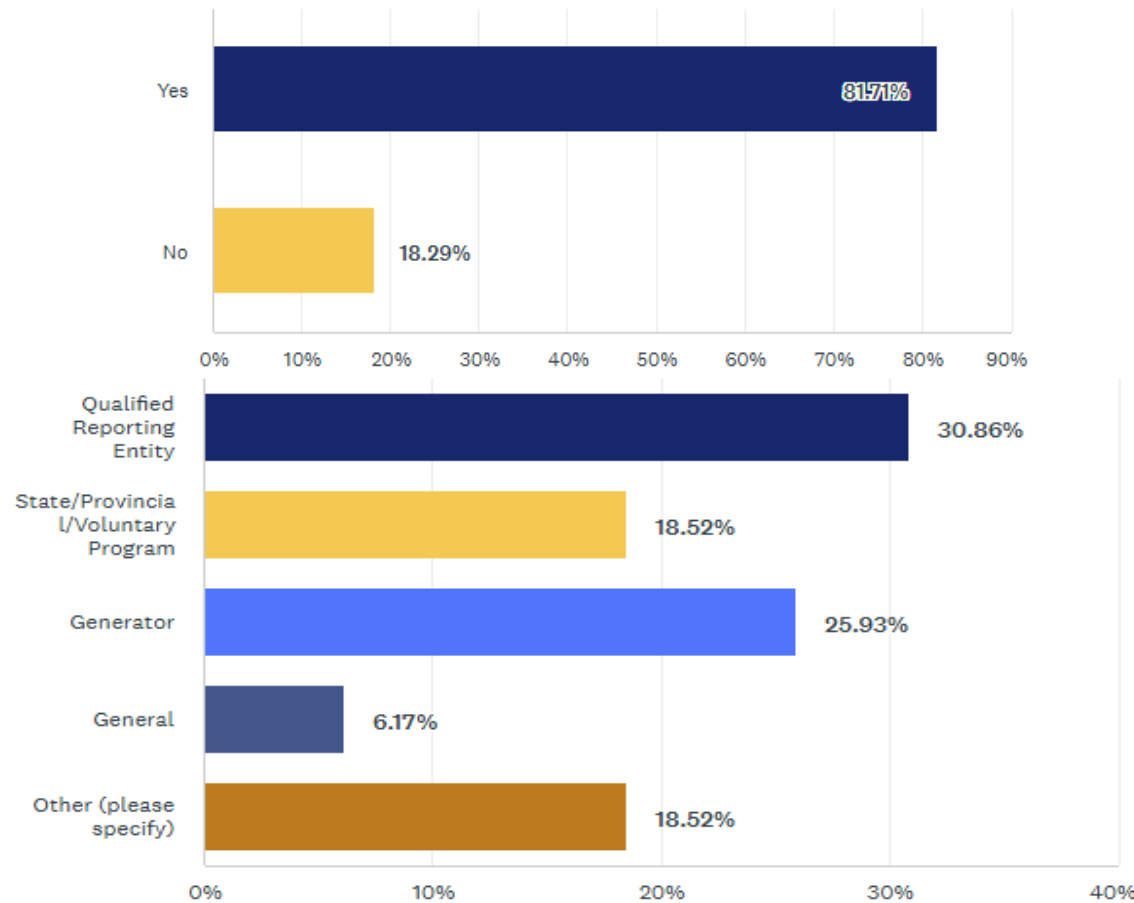


Which methods of information sharing have been most effective for you regarding WREGIS updates? Please select all that apply.

Answered: 77 Skipped: 6



# Draft Timeline for Separation and Stakeholder Engagement

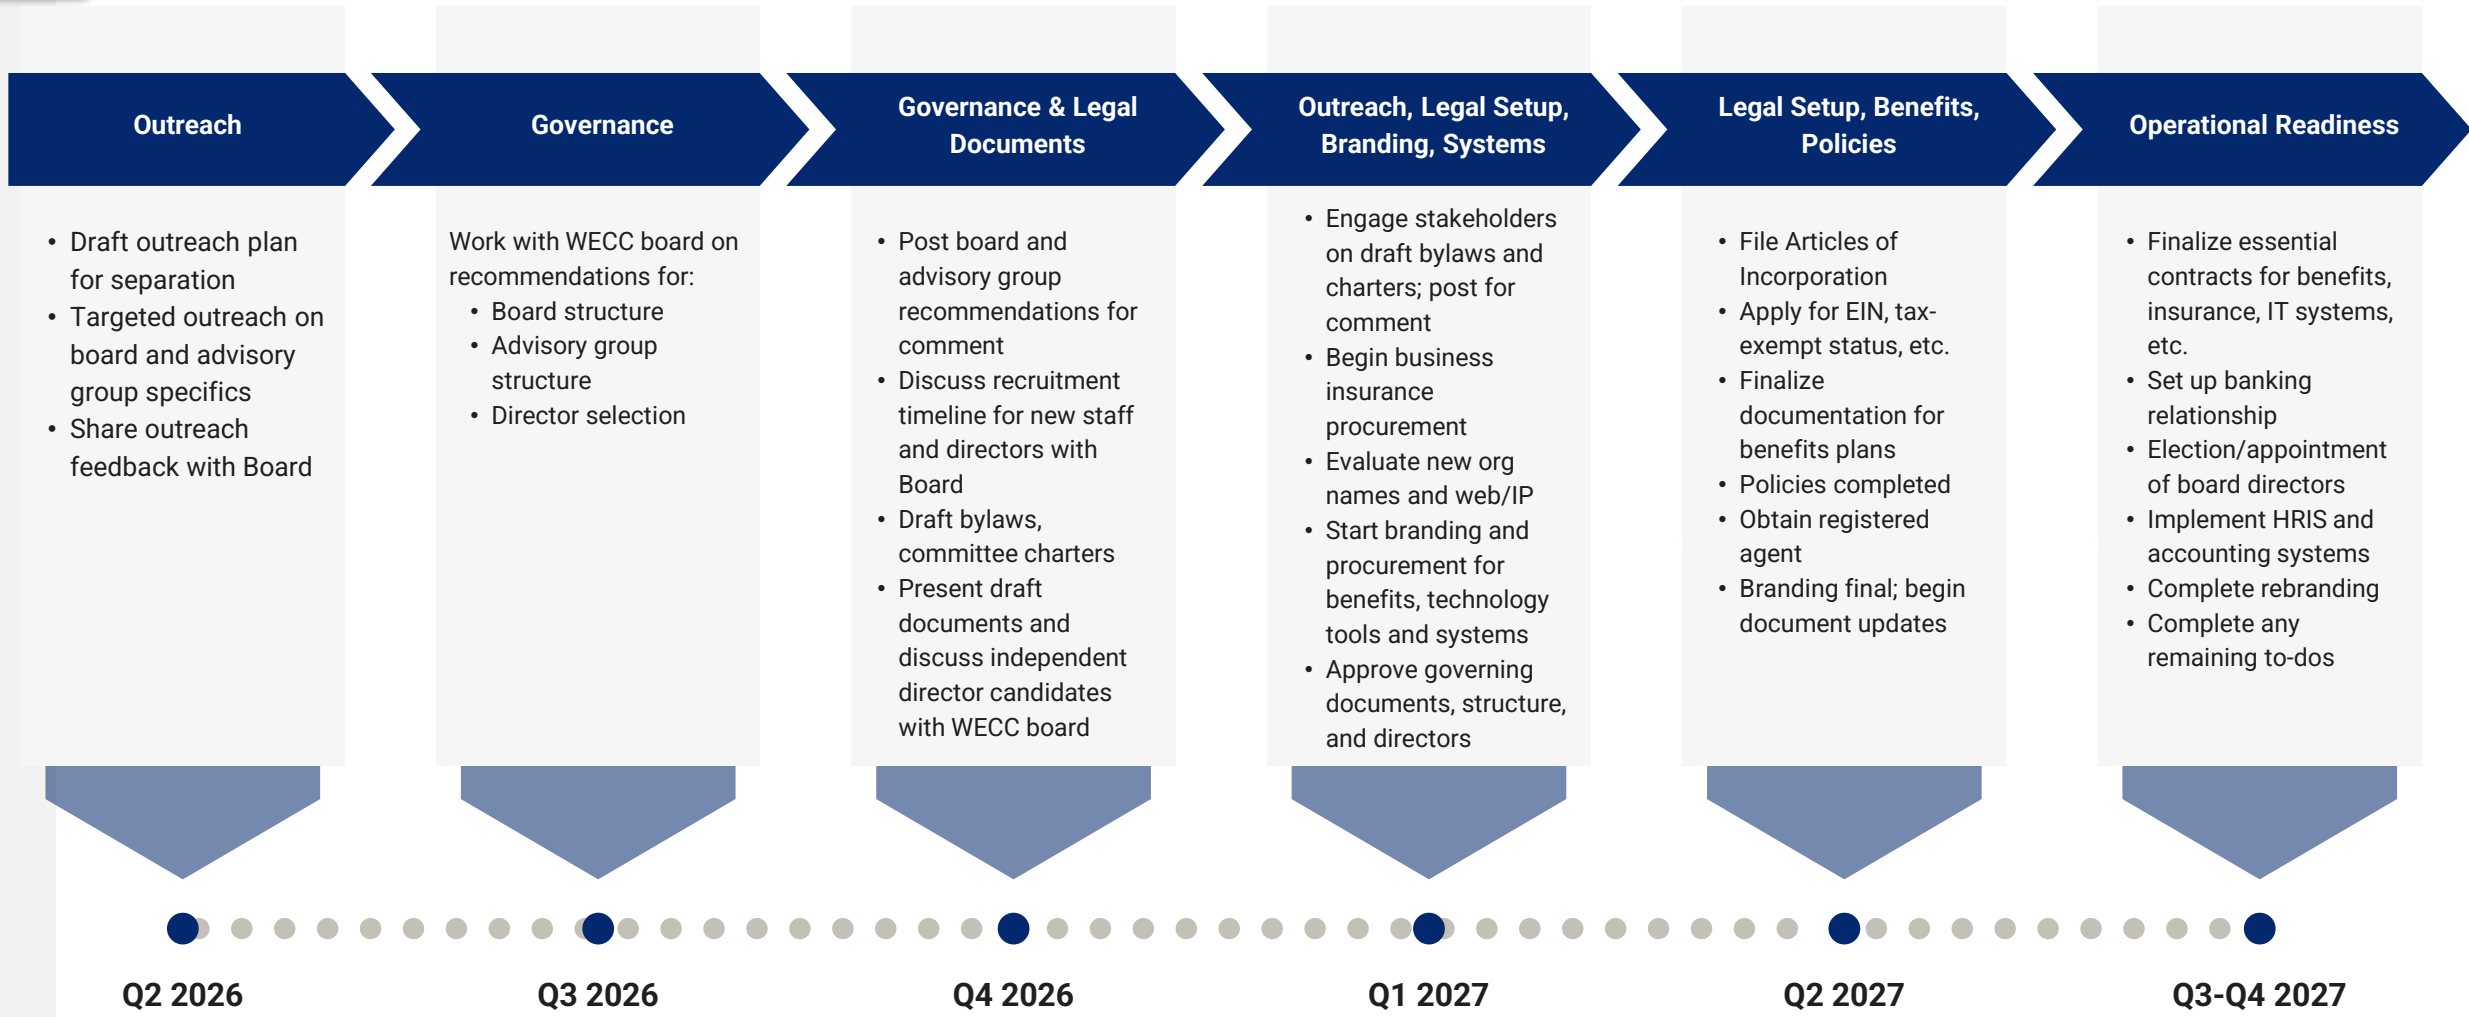


## January 1, 2028

- Transfer all WREGIS assets to the new organization
- Transition employees from WECC to the new organization



# Upcoming Events

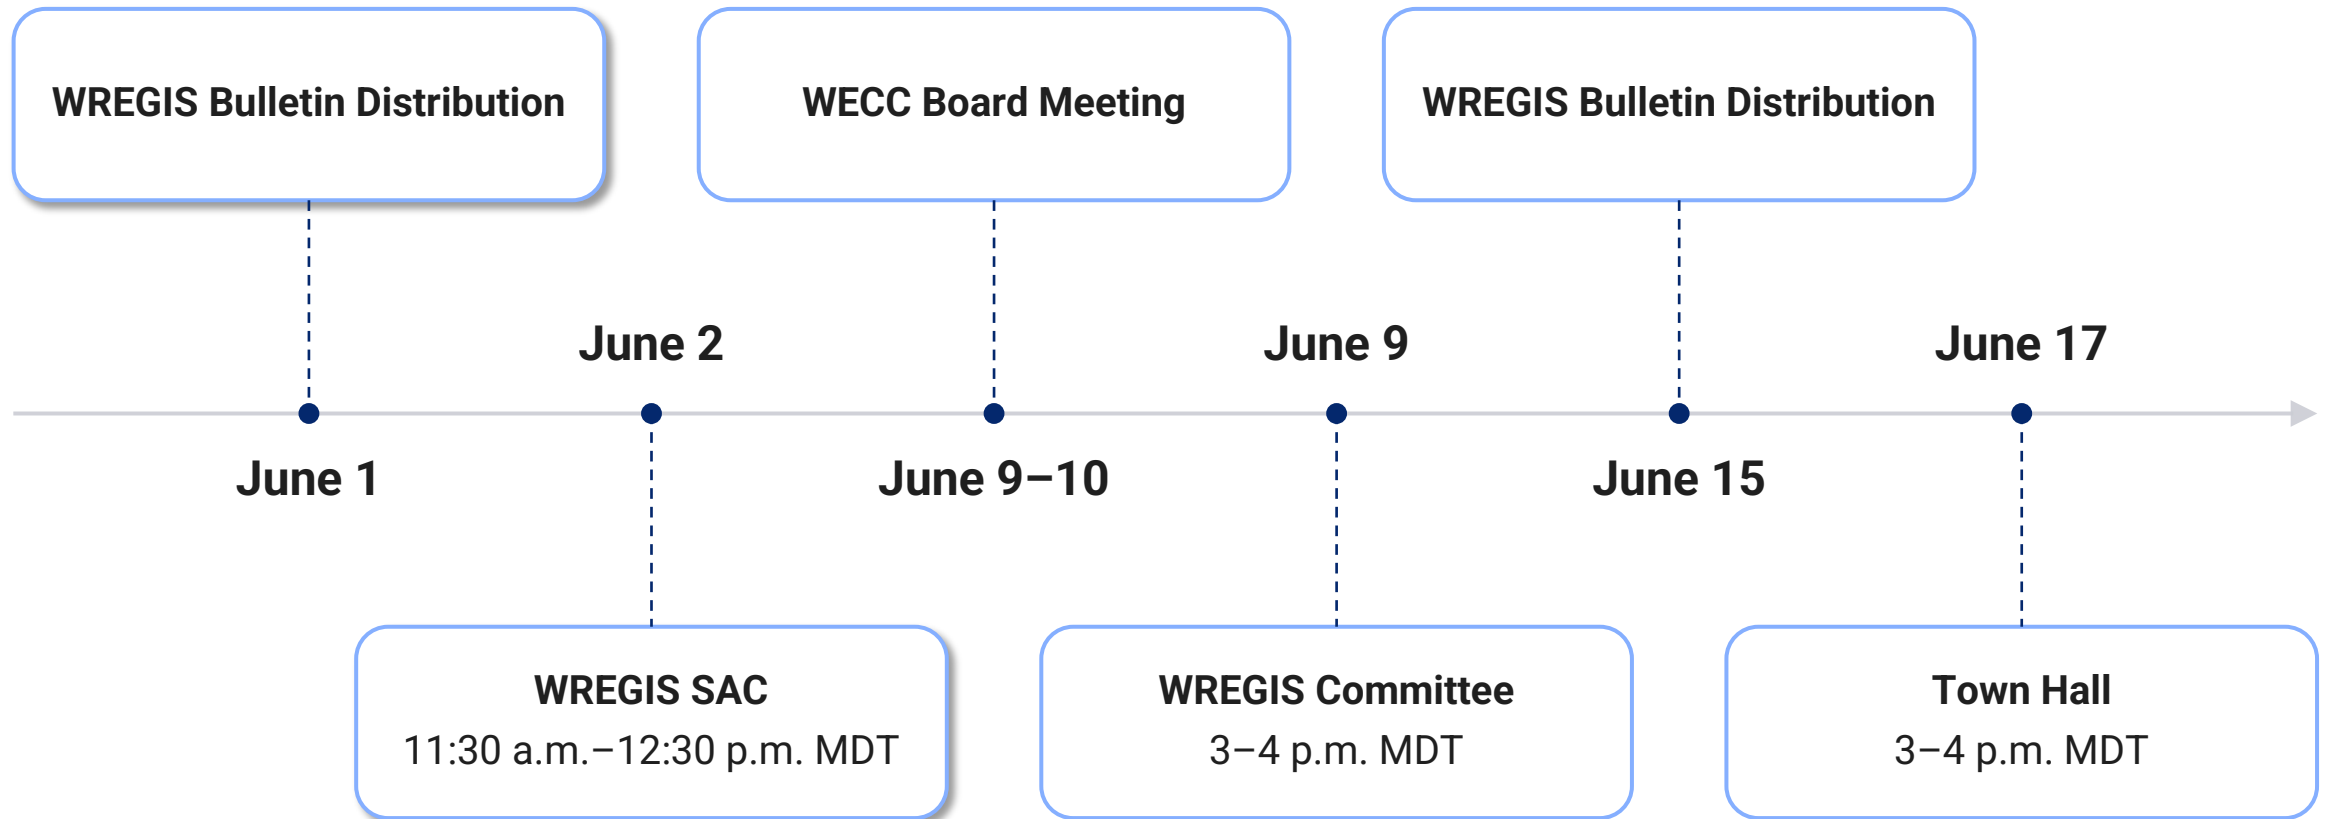



[engage@wecc.org](mailto:engage@wecc.org)



[www.wecc.org](http://www.wecc.org) | 801-582-0353



155 N 400 W, Salt Lake City, Utah 84103, USA
